Approved For Release 2002/06/17 : CIA-RDP78B04747A001500040055-2

CONFIDENTIAL

99824/5

17 February 1967
Ref: LJC 636-1674

Post Office Box 8043
Southwest Station
Washington, D.C. 20024

25X1A Attention: [redacted]
Contracting Officer

25X1A Reference: [redacted]

Dear Sir:

In accordance with the terms of the contract, we are transmitting herewith two (2) copies of Progress Report No. 6, Phase II, which covers the period January 1, 1967, through January 31, 1967.

Very truly yours,

ORIGINAL SIGNED BY

[redacted] 25X1A
Contracts

LJC/cc
encls. (2)

DECLASS REVIEW by NIMA/DOD

3cc: Progress Report No. 6, Phase II, to:

25X1A [redacted]
Post Office Box 8031
Southwest Station
Washington, D.C. 20024

*This Document contains information affecting the National Defense of the United States within the meaning of the Espionage Laws, Title 18, U.S.C., Sections 793 and 794, the transmission or revelation of which in any manner to an unauthorized person is prohibited by law.

EXCLUDED FROM AUTOMATIC REGRADING: DOD DIR 5200.10 DOES NOT APPLY

CONFIDENTIAL

Approved For Release 2002/06/17 : CIA-RDP78B04747A001500040055-2

Approved For Release 2002/06/17 : CIA-RDP78B04747A001500040055-2

25X1A

PROGRESS REPORT NO. 6
PHASE II

Report Period - 1/1/67 - 1/31/67

MULTI-PURPOSE DATA BLOCK READER

25X1A

Submitted by: [redacted]

Program Manager

Approved For Release 2002/06/17 : CIA-RDP78B04747A001500040055-2

Approved For Release 2002/06/17 : CIA-RDP78B04747A001500040055-2

A. CURRENT STATUS

All connectors have been received, although one week late. The succeeding critical tray wiring activity of six weeks has started and is expected to be completed within five weeks, thereby absorbing any other potential slippage. No problem is anticipated since there is a technician activity where overtime may be scheduled as required.

The two rewinders have been received two weeks ahead of schedule.

Fabrication of the transports for Units No. 1 and No. 2 have been completed on schedule. Panel wiring on Unit No. 1 has started on schedule.

B. PROJECTED WORK

Unit No. 1 - Tray and panel wiring will be completed. Electrical assembly will be completed.
Unit No. 2 - Tray wiring will start

C. ACTION ITEM

A test film is required from the Customer by March 24th if the present Fairchild delivery schedule is to be complied with. This date will be the final debugging period for Unit No. 1 in preparation for Acceptance Testing. 25X1A

Approved For Release 2002/06/17 : CIA-RDP78B04747A001500040055-2

Approved For Release 2002/06/17 : CIA-RDP78B04747A001500040055-2

25X1A

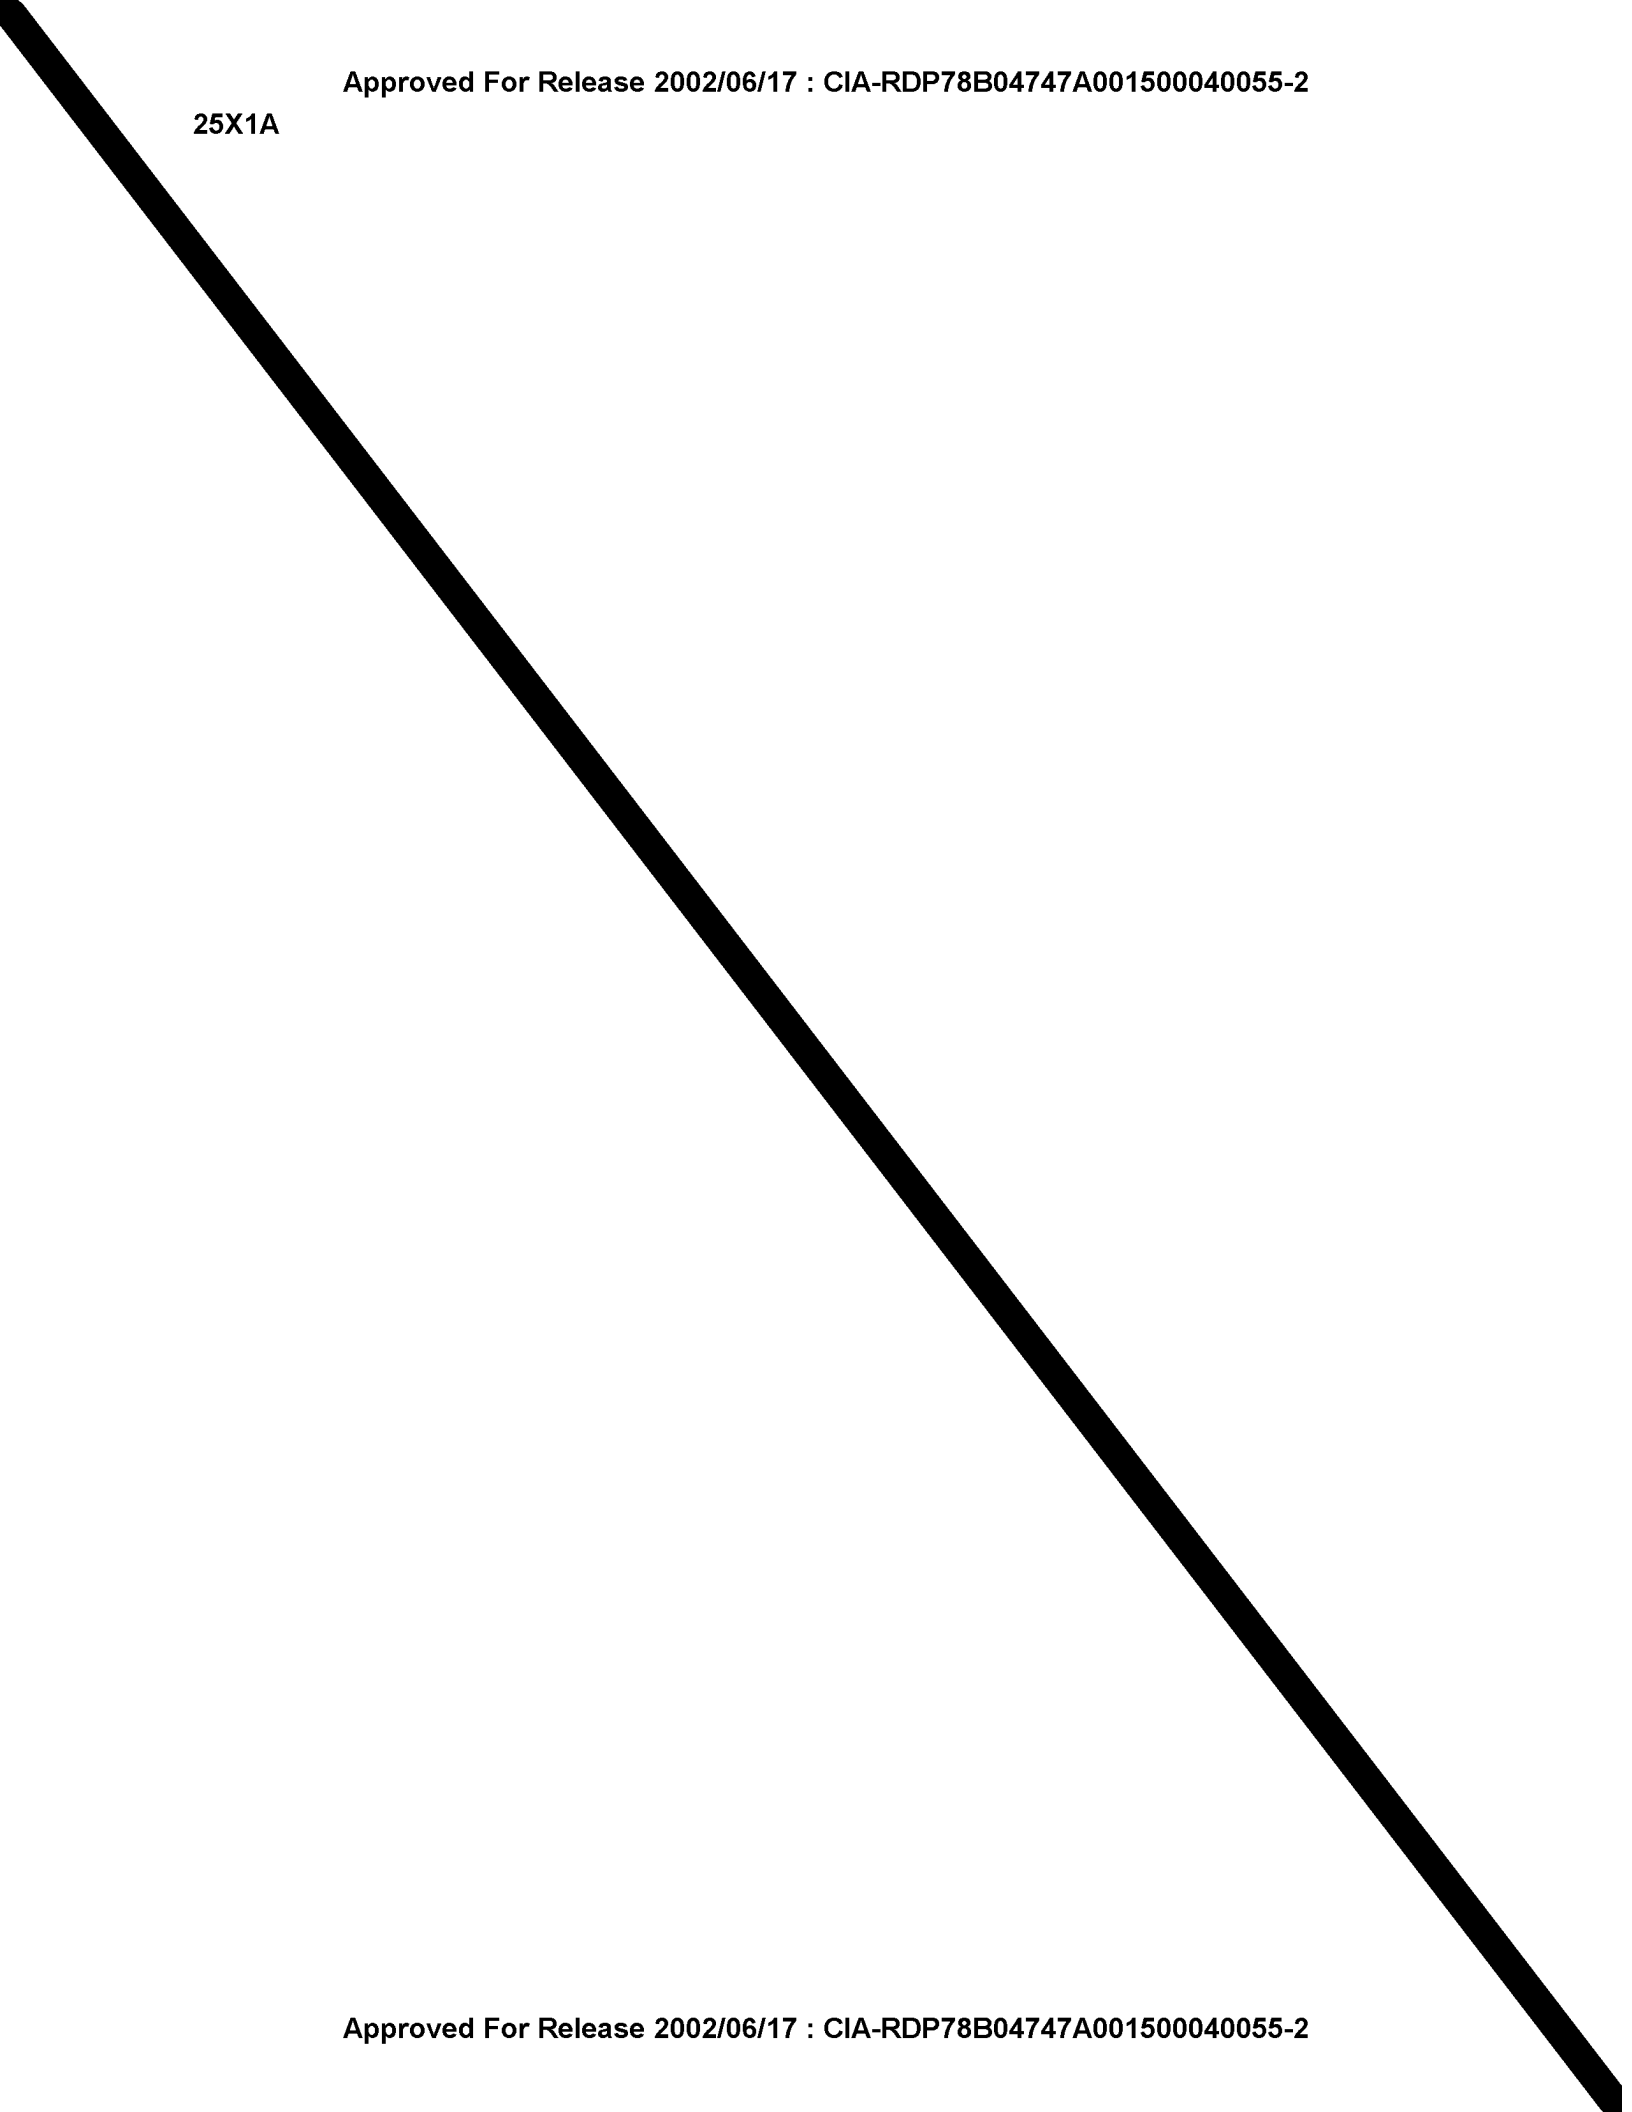

Approved For Release 2002/06/17 : CIA-RDP78B04747A001500040055-2
